


District of Columbia Clean Water Construction-State Revolving Fund (CWC-SRF) Site Summary

Schoolyard and Parkland Stormwater Retrofits			Grant Funding Year(s) FY2015	
RiverSmart Schools: Hart MS			Lead Agency DOEE	
			Project Type Design/Construction	
Infrastructure Type Green	Project Category School/Recreational Facility Retrofit	Address 1503 10th Street NW	Status Complete	
Design Start/End April 2017 – May 2017		Construction Start/End June 2017 – August 2017		
Objective Manage stormwater through bioretention basins and implementation of conservation landscaping while also offering educational opportunities to demonstrate the hydrological cycle and the importance of pollinators in the environment; and establish an outdoor classroom.				
Outputs <ul style="list-style-type: none"> • Designs and permits • 2 bioretention areas • Outdoor classroom 				
Sewershed MS4	Watershed Potomac River	Subwatershed Oxon Run	Ward 8	
Outcomes				
Stormwater Treatment Volume	Contributing Drainage Area	Impervious Surface Removed	Trees Planted	Linear Stream Feet Restored
12,941 gallons	18,773 ft ²	2,332 ft ²	14	n/a

Preconstruction



Construction

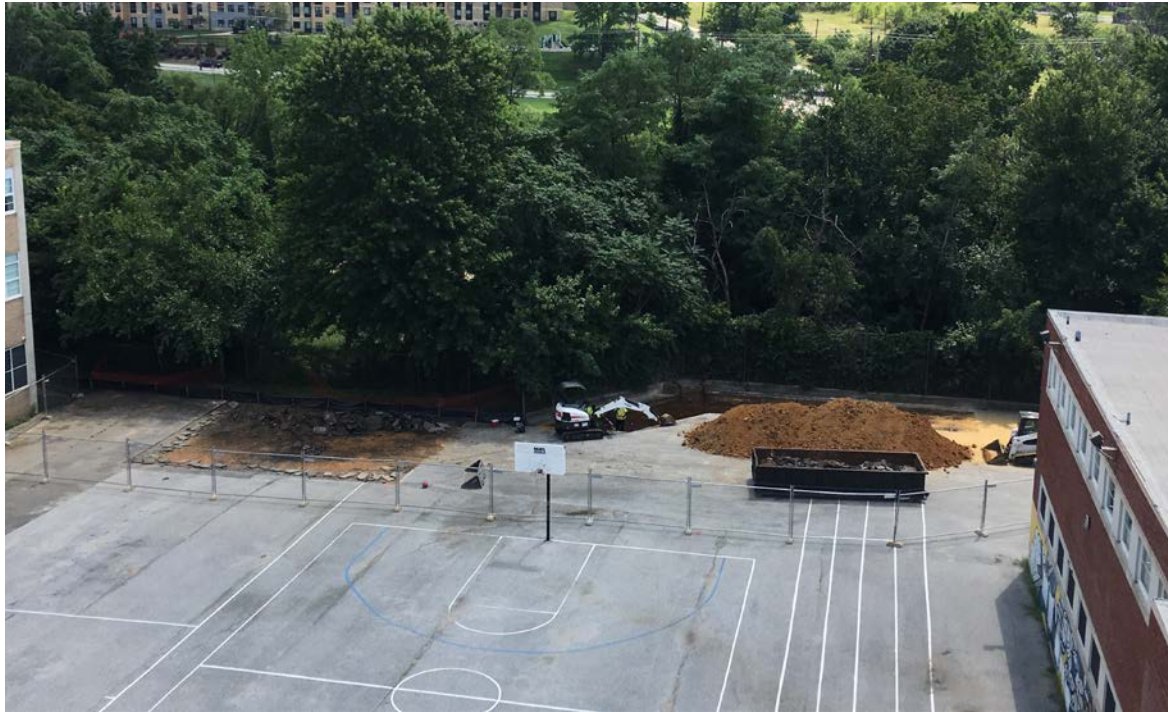

Completion

