

## RIVERSMART HOMES PERC TEST WORKSHEET

Name:	Address:

**Overview:** A percolation test, or perc test, determines how quickly water drains from the soil at a project site. If the soil does not drain within 36 hours, the project will not function properly and may lead to flooding on the property. Please follow steps 1-5 and fill out the *Perc Test Table* below. Avoid doing the perc test when raining. If the entire yard is paved, the test should be conducted as close to the project site as possible.

## **Materials Needed:**

- Digging tool (shovel or post-hole digger)
- Measuring tool (yard stick/ruler & reference stick)
- Water source (hose or bucket of water)
- Data collection tools (this worksheet & a pencil)


**Caution:** Make sure you know where utilities are before you start digging! Call Ms. Utility within 48 hours of digging to be sure.

**Step 1:** Dig a hole that is 24 inches deep and 6 inches wide in the area where the project will be installed.

**Step 2:** Fill up the hole with 12 inches of water and let it drain completely.

**Step 3:** Within 12 hours of the first fill draining, fill the hole again with 12 inches of water. Use the yardstick and reference stick/board to measure the water height every hour for 6 hours and record results in table.

**Step 4:** Follow the directions in the Perc Test Table to calculate the infiltration rate.

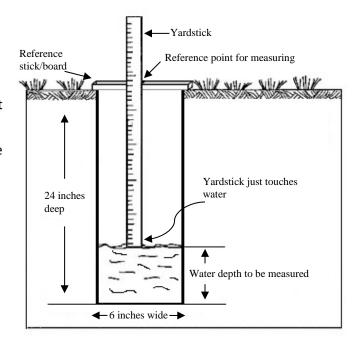

**Step 5:** Check the next day to make sure that the second filling has drained within 24-36 hours. An optimal infiltration rate is 1.2 inches per hour and minimum acceptable infiltration rate is .3 inches per hour – **if the hole has not drained within 36 hours a rain garden or pervious paver project is not possible.** 

## PERC TEST TABLE

Time	Elapsed Time (hours)	Depth of Water (inches)	Total Change in Water Level (inches)	Infiltration Rate (inches per hour)
First Fill :	0	12		
Second Fill :	1		Subtract water depth at hour 6 from 12 inches:	Divide total change in water level by 6 hours:
:	2			
:	3			
:	4			
:	5			
:	6			
	24		Water drained completely after :	hours

