ID		Task Mode	Task Name	Duration	Start	Finish	Predecessors
1			**Overall Project**	**121 days**	**Thu 4/12/18**	**Thu 9/27/18**	
2			1.0 Kickoff Meeting	1 day	Thu 4/12/18	Thu 4/12/18	
3			2.0 Data Request	20 days	Fri 4/13/18	Thu 5/10/18	2
4			3.0 Monthly Meetings (14) and Quarterly Meetings (3)	119 days	Fri 4/13/18	Wed 9/26/18	2
5			4.0 Analysis of Short-Term Measurement Data	30 days	Fri 5/11/18	Thu 6/21/18	3
6			5.0 Analysis and Mapping of Phase 1 AEDT Modeling	30 days	Fri 4/13/18	Thu 5/24/18	2
7			6.0 Analysis of 4 Weeks of 2017 Measurement Data	55 days	Fri 5/11/18	Thu 7/26/18	3
8			**7.0 Field Measurements During Spring/Summer 2018**	**100 days**	**Fri 4/13/18**	**Thu 8/30/18**	
9			7.1 Select Sites, Obtain Access	30 days	Fri 4/13/18	Thu 5/24/18	2
10			7.2 Measure Noise Levels for 30 Days	45 days	Fri 5/25/18	Thu 7/26/18	9
11			7.3 Data Analysis	50 days	Fri 6/1/18	Thu 8/9/18	10SS+5 days
12			7.4 Report	50 days	Fri 6/22/18	Thu 8/30/18	11SS+15 days
13			8.0 Analysis and Mapping of NMT Data	30 days	Fri 5/11/18	Thu 6/21/18	3
14			9.0 Public Meeting	10 days	Fri 8/31/18	Thu 9/13/18	12
15			10.0 Final Report	10 days	Fri 9/14/18	Thu 9/27/18	14

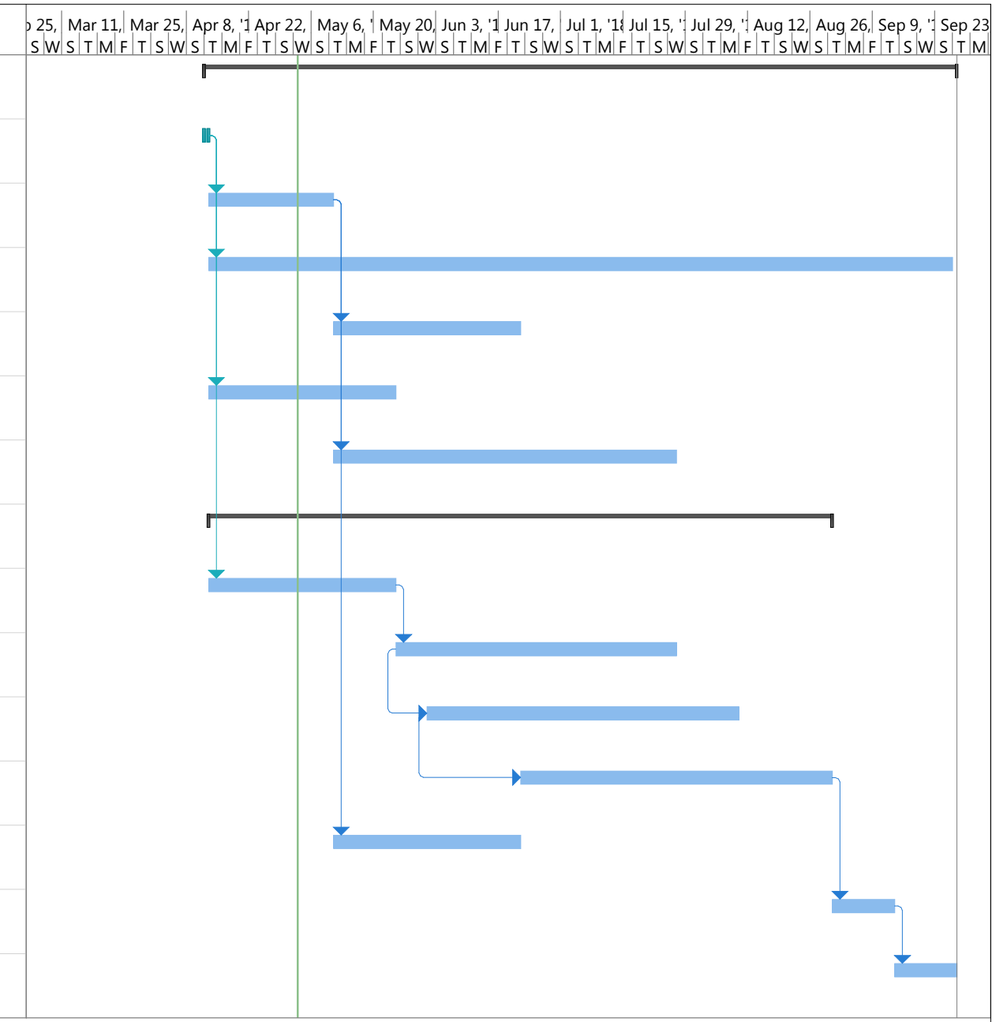

Project: DCA Noise Analysis
Phase 2
Date: Thu 5/3/18

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			
